



DRA ASTRA Construction update photos – October 2025



AREA

Total Land Area: 53143 SQFT
Total Saleable Area: 187894 SQFT
Total Build-up Area: 232430 SQFT



SCHEDULE

Start date : 03-Feb-25
End Date : 30-Oct-27
Total Month : 32 months 28 days



DURATION

Project Duration : 1000 Day's
Completed Day's: 270 Day's
Remaining Day's : 730 Day's




DWELLING UNITS

Total Units : 132 Units
2BHK + 2T : 30 Units
3 BHK + 2T : 51 Units
3 BHK + 3T : 51 Units
UG Sump Capacity : 70 KLD
STP capacity : 115 KLD




PROJECT DETAIL

- Stilt & Upper Stilt Parking.
- 2nd Floor to 12th Floor Residential.
- Foundation - Raft Foundation
- Amenities – 30+



DRA ASTRA – NEXT MILESTONES

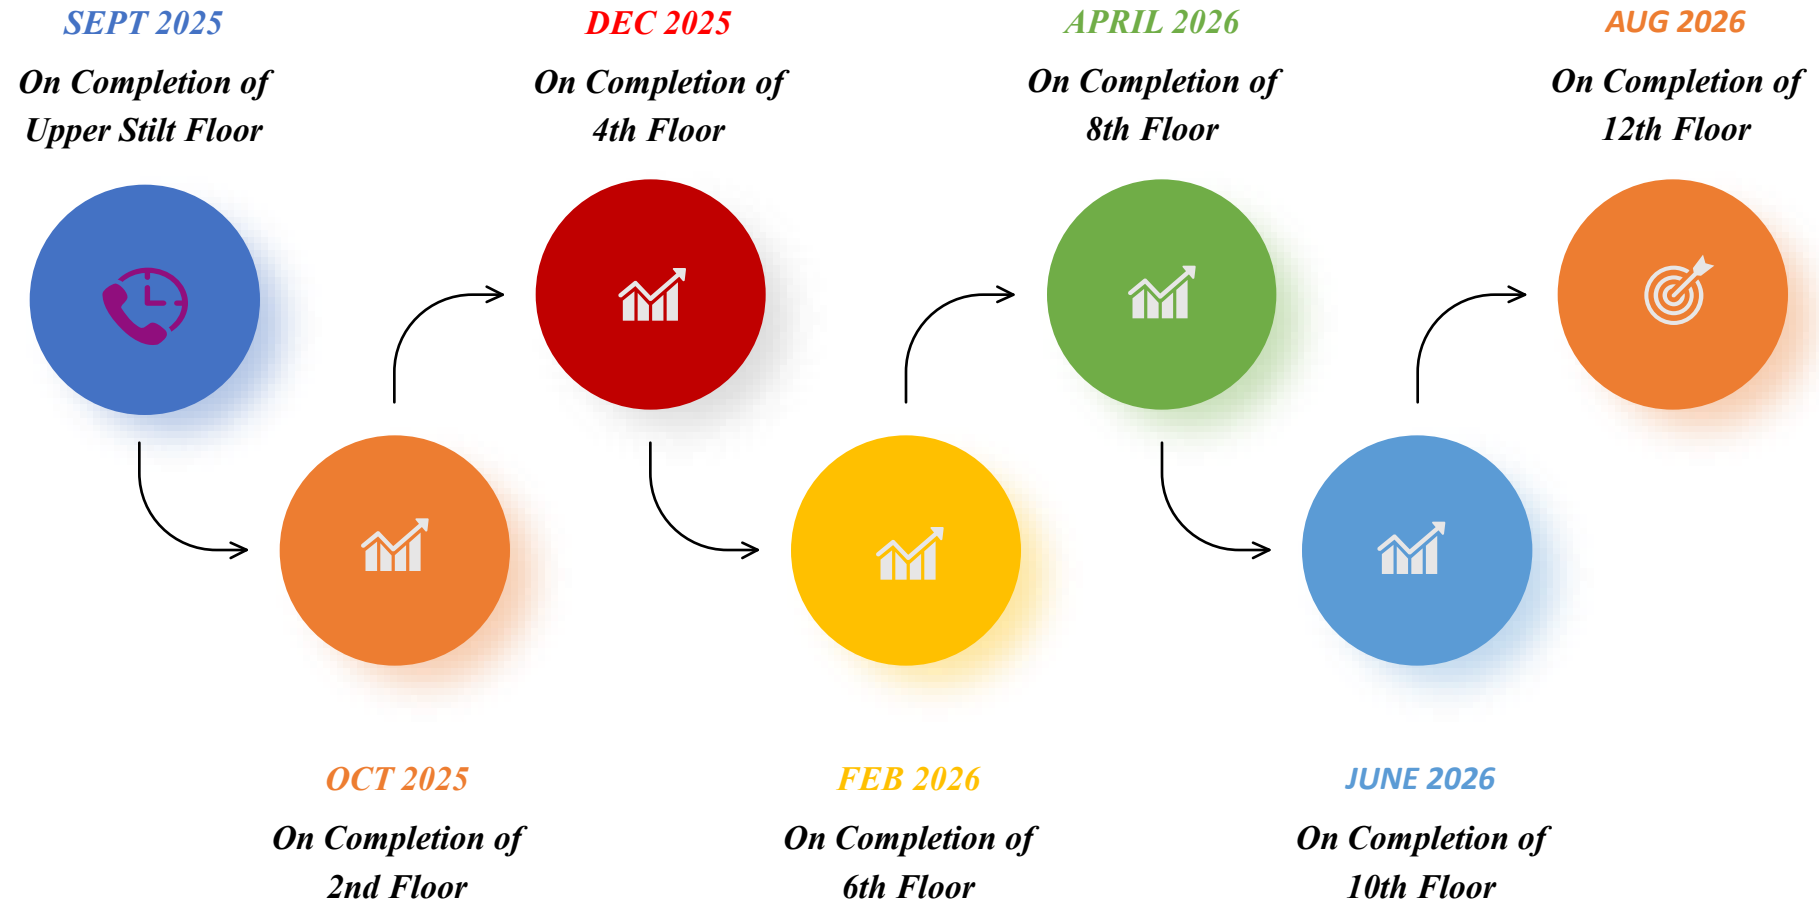

COMPLETION PERCENTAGE WEEKLY BASIS FOR OCTOBER MONTH

Description	Target	Achieved	55%
WEEK 1	0.25%	0.30%	60%
WEEK 2	0.25%	0.40%	80%
WEEK 3	0.25%	0.30%	60%
WEEK 4	0.25%	0.1%	20%


OCT-25
1ST
WEEK
13.30%

OCT-25
2ND
WEEK
13.70%

OCT-25
3RD
WEEK
14.00%

OCT-25
4TH
WEEK
14.10%

PROGRESS STATUS CHART

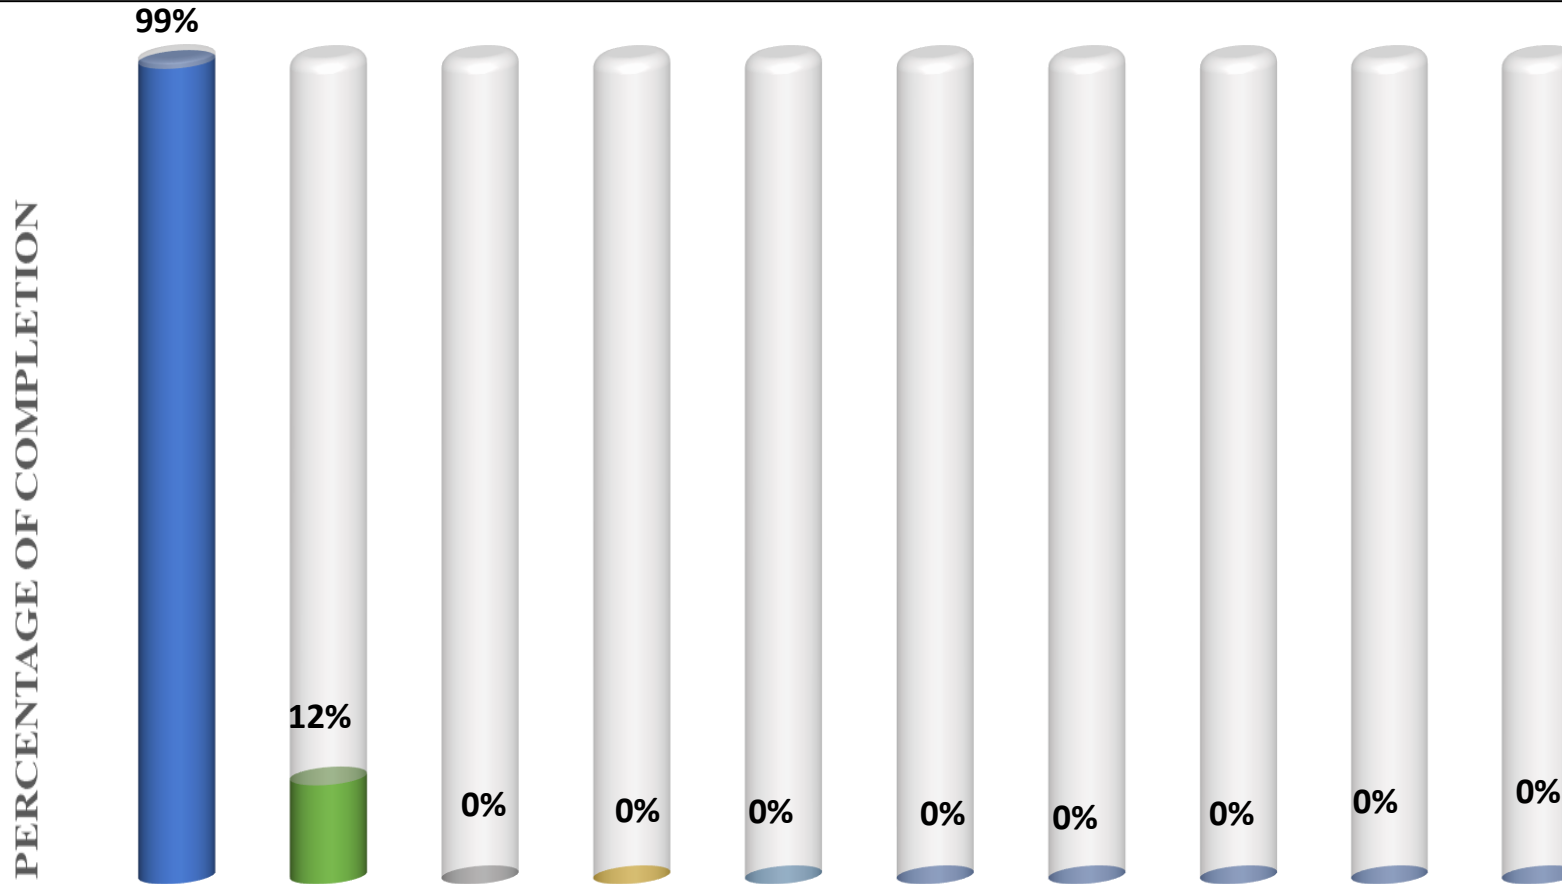

	Foundati on work	Structure work	Block work	Internal plasterin g	External plasterin g	Finishin g	Commnan area finishing	External painting	External develop ment	Handing over
■ Pending	1%	88%	100%	100%	100%	100%	100%	100%	100%	100%
■ Completed	99%	12%	0%	0%	0%	0%	0%	0%	0%	0%

TOP VIEW



27 October 2025 at 3:56 PM

27 October 2025 at 3:56 PM

Main building – Pour 2 stilt floor roof Slab balance area shuttering work completed



Main building – Pour 2 stilt floor roof Slab balance area Reinforcement work completed.



Main building – Pour 2 stilt floor roof Slab balance area Concrete work completed



Main building – Pour 2 Exist ramp reinforcement work completed.



Main building – Pour 2 Exist ramp concrete work completed



Main building – Pour 1 - 1st floor roof slab shuttering work completed.



Main building – Pour 1 – 1st floor slab reinforcement work completed.



26 October 2025 at 5:03 pm

26 October 2025 at 5:03 pm

Main building – Pour 1 - 1st floor slab Outer side board and projection work in progress.



Main building – Pour 2 first floor column reinforcement work in progress (45 Nos / 69 Nos)



Main building – Pour 2 first floor column shuttering work in progress (31 Nos / 69 Nos)



Main building – Pour 2 first floor column concrete work in progress (28 Nos / 69 Nos)



27 October 2025 at 2:47 pm

27 October 2025 at 2:47 pm

Tower crane counter weight shuttering and reinforcement work completed.



Tower crane counter weight concrete work completed.



Tower crane erection work in progress.



Tower crane erection work in progress.



South side road formation work done for vehicle access.



*Thank
you!*
