



DRA ASTRA Construction update photos – March 2025

Over all percentage of Completion

S. No	Project Code	Project Name	Saleable Area in Sqft	Cumulative% Achieved up to March-25	Status
1	DRA-30`	Astra	1,87,894	3%	Foundation Stage



Main building – Pour 1 Raft concrete work completed (509cum)



Main building – Pour 1 & 2 DPC primer Applied on column



Main building – Pour 2 raft reinforcement work completed



Main building – Pour 2 raft shuttering work completed



Main building – Pour 2 raft concrete 550 cum completed



Main building – Pour 2 raft concrete power trowel finishing work completed



Main building – Pour 2 raft curing bund construction work completed



Main building – Pour 2 Raft de-shuttering work completed



Main building – Pour 2 column shuttering work completed (28/28 no's)



Main building – Pour 3 Raft PCC work completed



Main building & UG Sump – Raft PCC work completed



UG sump & Main building pour 3 raft reinforcement work completed




UG Sump & main building pour 3 raft concrete work completed (515.5 cum)



UG Sump & main building pour 3 raft concrete floating work completed



Main building – Pour 4 raft excavation work in progress

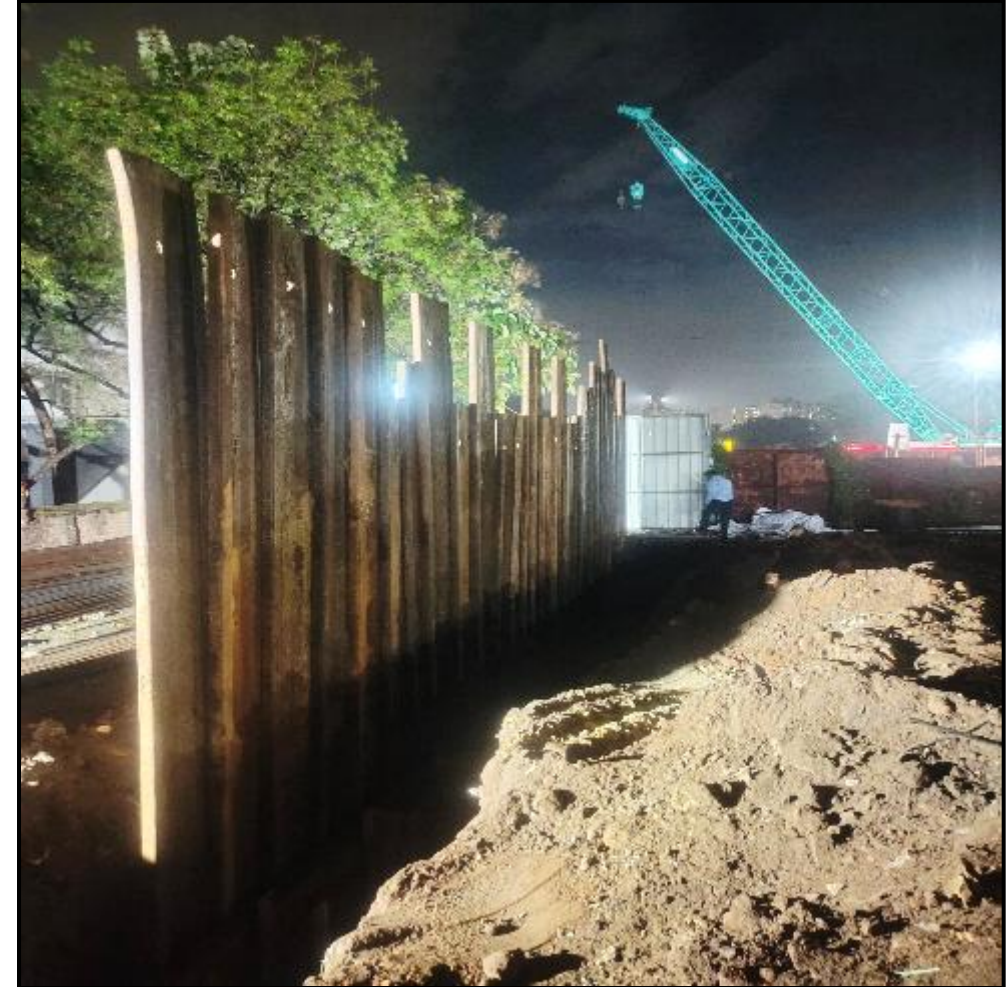

STP Shoring work in progress

*Thank
you!*
