



DRA ASTRA Construction update photos – November 2025



AREA

Total Land Area: 53143 SQFT
Total Saleable Area: 187894 SQFT
Total Build-up Area: 232430 SQFT



SCHEDULE

Start date : 03-Feb-25
End Date : 30-Oct-27
Total Month : 32 months 28 days



DURATION

Project Duration : 1000 Day's
Completed Day's: 300 Day's
Remaining Day's : 700 Day's




DWELLING UNITS

Total Units : 132 Units
2BHK + 2T : 30 Units
3 BHK + 2T : 51 Units
3 BHK + 3T : 51 Units
UG Sump Capacity : 70 KLD
STP capacity : 115 KLD




PROJECT DETAIL

- Stilt & Upper Stilt Parking.
- 2nd Floor to 12th Floor Residential.
- Foundation - Raft Foundation
- Amenities – 30+



DRA ASTRA – NEXT MILESTONES

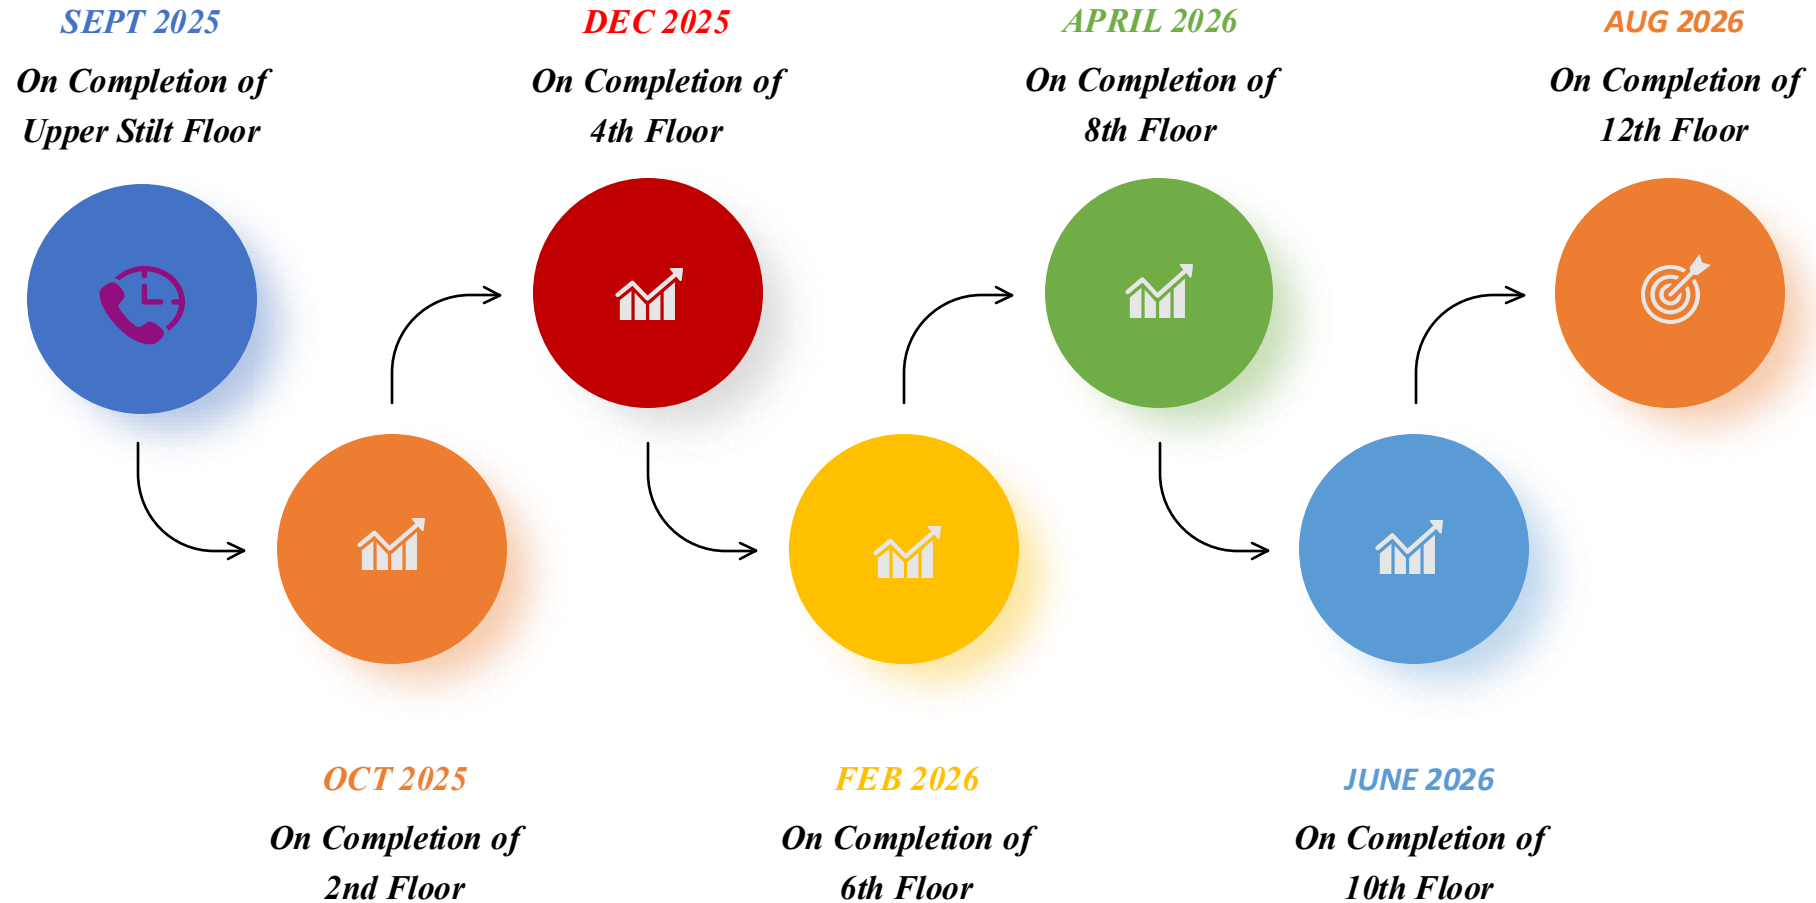

COMPLETION PERCENTAGE WEEKLY BASIS FOR NOVEMBER MONTH

Description	Target	Achieved	65%
WEEK 1	0.25%	0.1%	40%
WEEK 2	0.25%	0.15%	60%
WEEK 3	0.25%	0.20%	80%
WEEK 4	0.25%	0.20%	80%

NOV-25
1ST
WEEK
14.30%


NOV-25
2ND
WEEK
14.45%

NOV-25
3RD
WEEK
14.65%

NOV-25
4TH
WEEK
14.85%

PROGRESS STATUS CHART

PERCENTAGE OF COMPLETION

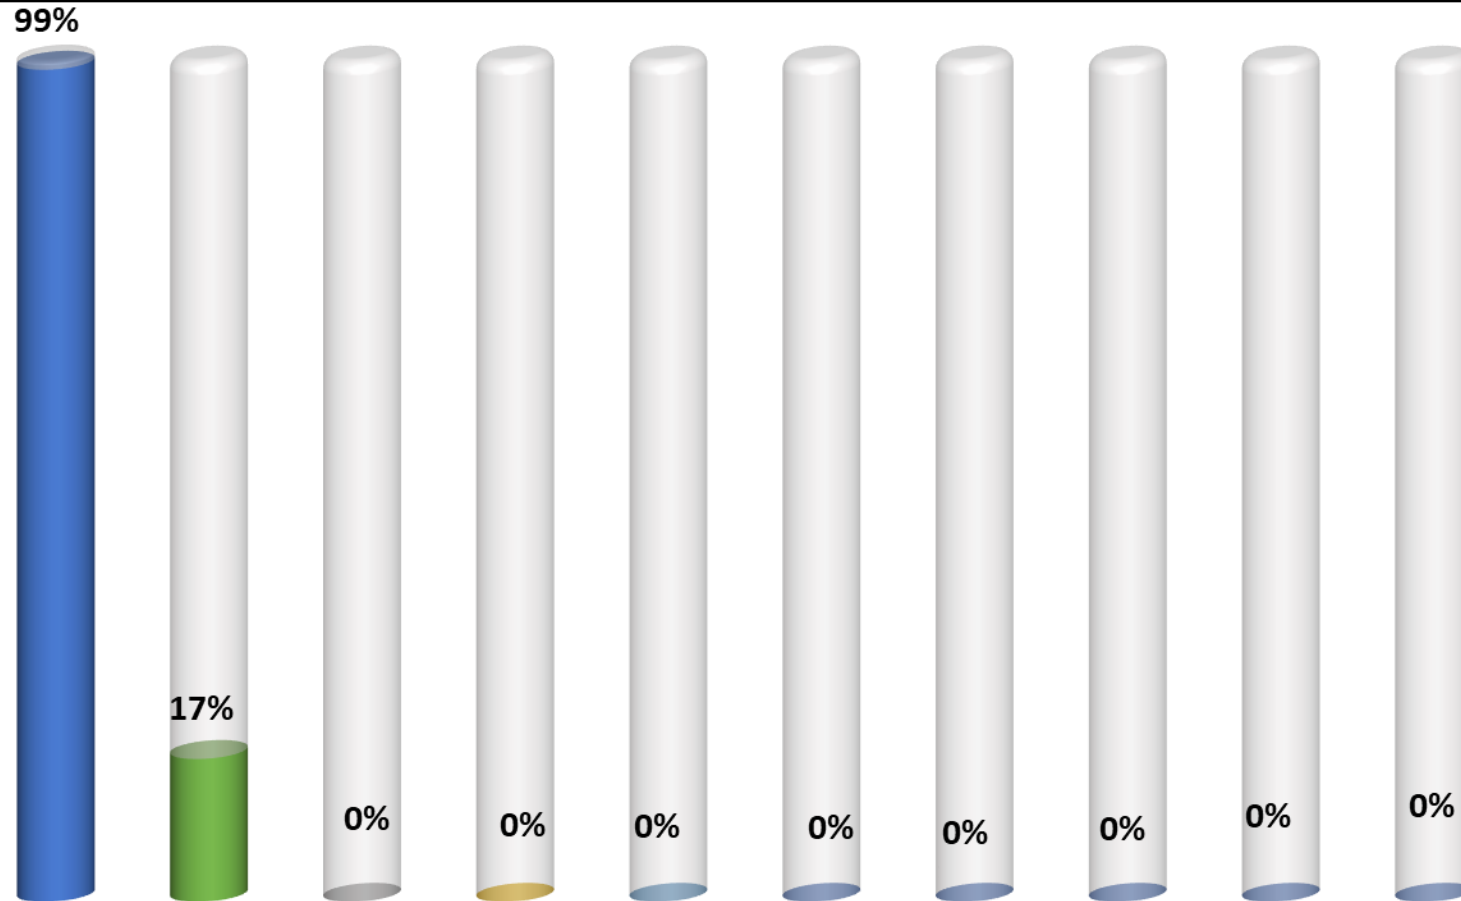

	Foundati on work	Structure work	Block work	Internal plasterin g	External plasterin g	Finishin g	Comman area finishing	External painting	External develop ment	Handing over
■ Pending	1%	83%	100%	100%	100%	100%	100%	100%	100%	100%
■ Completed	99%	17%	0%	0%	0%	0%	0%	0%	0%	0%





SOUTHEAST SIDE ELEVATION



SOUTHWEST SIDE ELEVATION



PROGRESS PHOTOS

SOUTHWEST SIDE ELEVATION



NORTH WEST SIDE ELEVATION





**Main building – Pour 2 – 1st floor column concrete completed
(69 Nos / 69 Nos)**



Main building – Pour 2 – Stilt floor roof slab de-shuttering work



Main building – Pour 2 – 1st floor roof slab shuttering work



Main building – Pour 2 – 1st floor roof slab beam reinforcement work



Main building – Pour 2 – 1st floor roof slab reinforcement work



Main building – Pour 2 – 1st floor roof slab concrete work



**Main building – Pour 1 – 2nd floor column & lift shuttering completed
(57 Nos / 57 Nos) .**



**Main building – Pour 1 – 2nd floor slab column concrete completed
(57 Nos / 57 Nos)**



Main building – Pour 1 – 2nd floor roof slab shuttering work in progress.

TOP VIEW

DRA ASTRA

12:59:19 PM

PROJECT COUNTDOWN

DAYS HRS MINS SECS

700:11:00:39

PROJECT START DATE : 01/02/2025

COMPLETION DATE : 31/10/2027

HAVE A NICE DAY

*Thank
you!*
