



DRA COVE

Monthly Construction Updates – November 2025



S.No.	Work Description	% Of Completion
Internal flat - Plumbing Work Progress		
1	8th floor Toilet Plumbing Water line Pipe fixing work Completed	90%
2	8th floor Toilet Plumbing Water line Pressure Test work Completed	90%
3	8th floor Toilet Plumbing Flush Tank fixing work Completed	90%
4	9th floor Toilet Plumbing Water line wall chasing work Completed	90%
5	10th floor Toilet Plumbing Water line wall chasing work Completed	90%
6	11th floor Toilet Plumbing Water line pipe fixing work in progress	40%
7	12th floor Toilet Plumbing Water line pipe fixing work Completed	90%
Internal flat - Firefighting Work Progress		
1	8th, 9th floor - Corridor Firefighting work Testing work in progress	90%
2	10th, 11th, 12th floor - Corridor Firefighting work Testing work in progress	25%

S.No.	Work Description	% Of Completion
Internal flat - Waterproofing Work Progress		
1	8th floor Toilet Sunkan filling work in progress	30%
2	12th floor Toilet Waterproofing - Coating Completed	90%
3	11th floor Toilet Waterproofing - Surface Preparation work in progress	40%
Internal flat - Electrical Work Progress		
1	8th to 12th floor Electrical wall chasing and Box, Pipe fixing work completed	90%
2	8th to 12th floor Corridor Electrical Tray fixing work completed	90%
Internal flat - Suit Room Work Progress		
1	8th to 12th floor Suit Room Toilet Partition wall Block work and Plastering work Completed	75%
External - Work Progress		
1	External West Side Wall Painting work in progress	40%
2	Terrace South Side Logo Signage board Installation work completed	90%
3	External Chequer Plate welding fixing work Completed	90%
4	External AC Drain line Vertical and Horizontal line connection work in progress	75%
5	Lift No.1 Railing Erection work in progress	75%
6	External Façade Glass Silicon work completed	90%
7	Common area Firefighting Commissioning work in progress	40%



Site Front View


Flat No.802 Interior Work Completed



Flat No.803 Painting Work Completed



8th, 9th, 10th, 11th floor Suit Room Toilet Plastering work completed

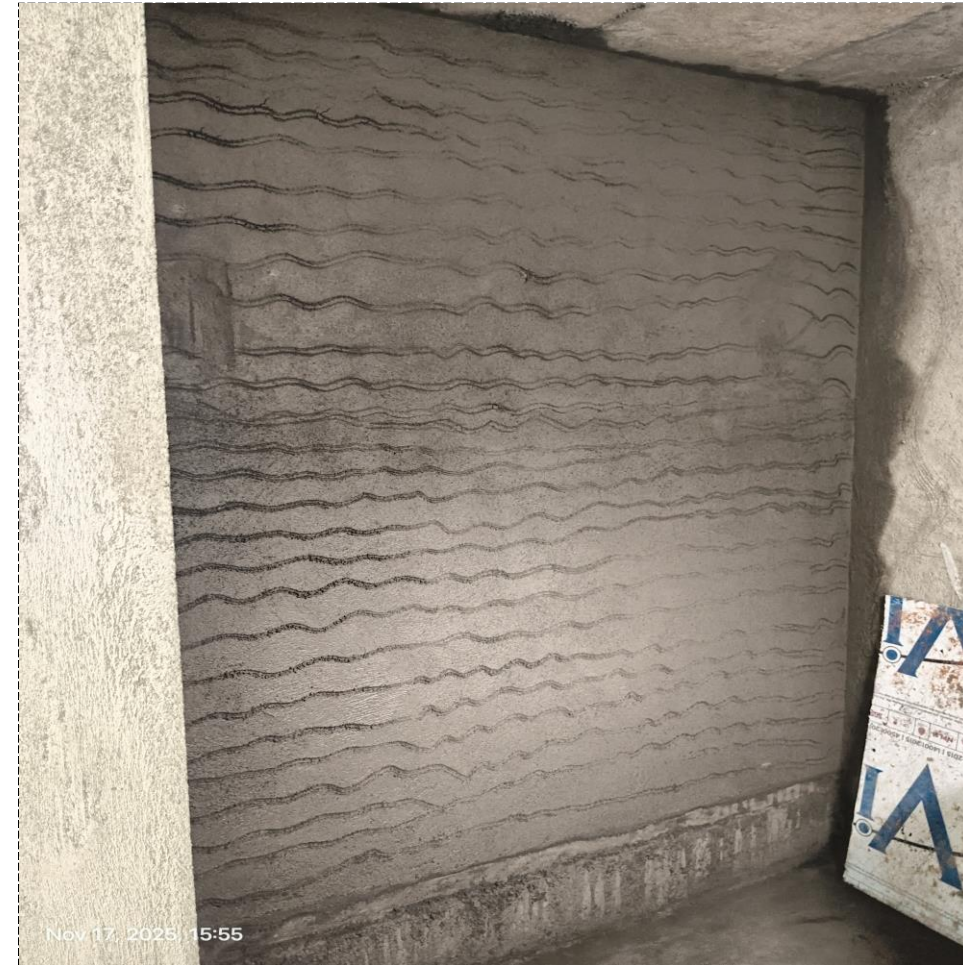

Terrace Floor Logo Board Base Concrete and Plastering Work Completed



8th Floor Kitchen Plumbing Pipe Fixing Work Completed



8th floor Toilet Plumbing water line and Tank fixing work in progress



9th to 12th floor Toilet Plumbing water line pipe fixing work In Progress



8th floor Electrical Box and DB fixing work completed



Electrical Tray Fixing Work In Progress




11th & 12th floor Electrical Wall chasing and pipe fixing completed



10th floor Electrical Wall chasing and pipe fixing and DB fixing Work In Progress



Staircase No.2 - 12th floor UPVC window installation work completed

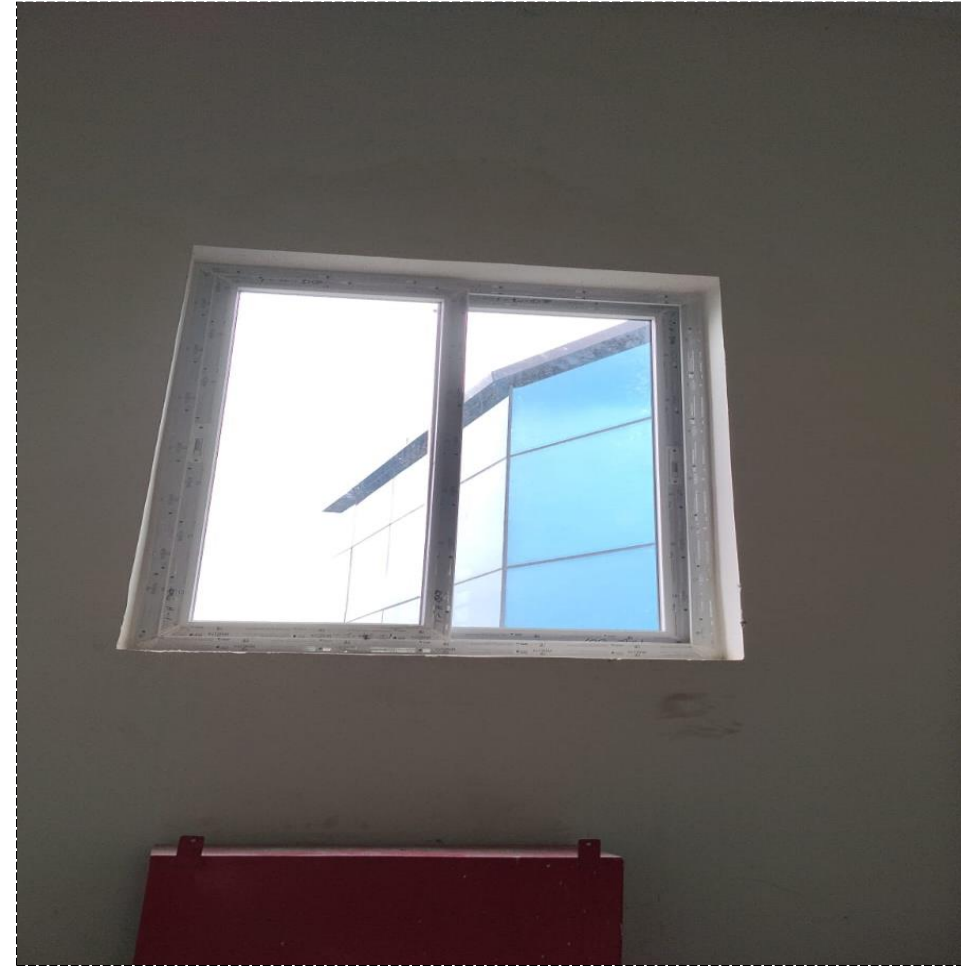

Lift No.1 Erection work in progress



8th to 12th AC Outdoor MS Plate Work Completed





AC Outdoor unit – MS Plate – Handrail Work In Progress



External Air Crack and Primer Work In Progress



Logo Fixing Work Completed



Thank you!
