



DRA HARMONY

CONSTRUCTION UPDATES - MARCH 2025

Over all percentage of Completion

S. No	Project Code	Project Name	Saleable Area in Sqft	Cumulative% Achieved up to March-25	Status
1	DRA-19	Harmony	1,88,014	72%	Structure & Finishing Ongoing

STAGE COMPLETION STATUS UP TO MARCH -25

S. No	Description	Status	% of Completion	Remarks
1	Completion of Foundation	Completed	100%	
2	Completion of Stilt Floor Roof	Completed	100%	
3	Completion of Upper Stilt Floor Roof	Completed	100%	
4	Completion of First Floor Roof	Completed	100%	
5	Completion of Third Floor Roof	Completed	100%	
6	Completion of Fifth Floor Roof	Completed	100%	
7	Completion of Seventh Floor Roof	Completed	100%	
8	Completion of Ninth Floor Roof	Completed	100%	
9	Completion of Eleventh Floor Roof	Completed	100%	
10	Completion of Thirteenth Floor Roof	Completed	100%	
11	Completion of Masonry Work	Upto 12 th Floor Completed	100%	
12	Completion of Internal Plastering	Upto 10 th Floor Completed	55%	
13	Completion of Internal Finishes	Work In Progress	55%	Tiling & Painting Work In progress



West side Elevation



East Side Elevation



South Side Elevation



North Side Elevation



Thirteenth Floor Roof Slab Concrete Work Completed



Terrace Parapet Wall Block Work In Progress




Twelfth Floor Block Work



Tenth Floor Plastering Work Completed



Eleventh Floor Plastering Work In Progress

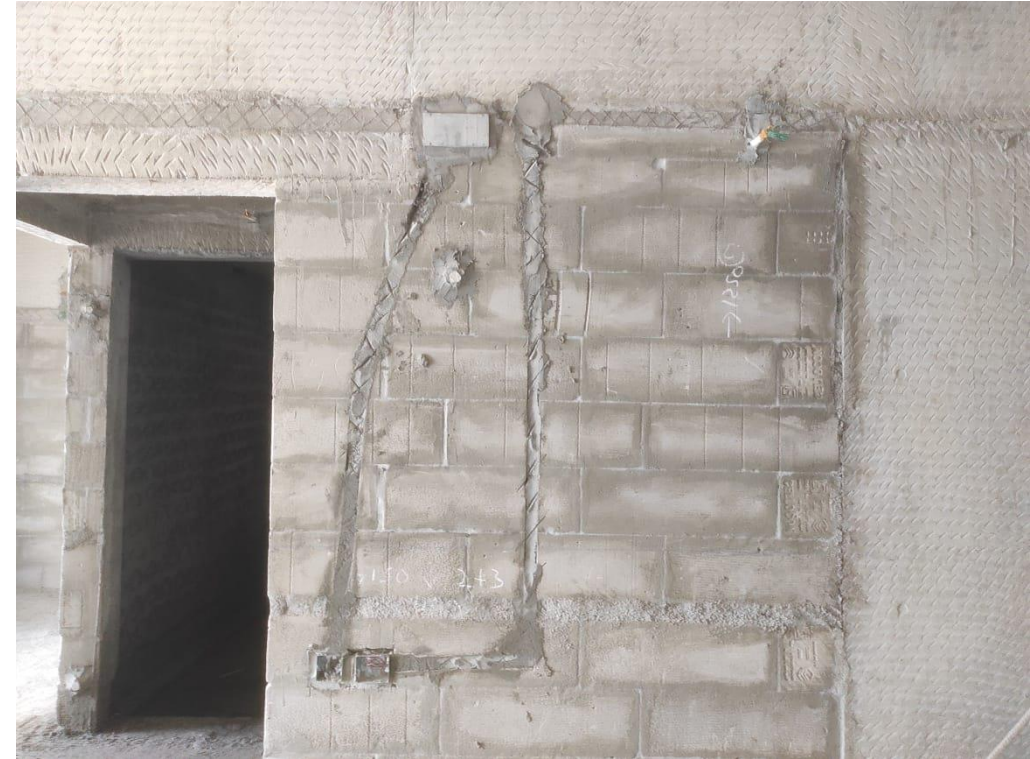

Electrical –Eleventh Floor Electrical Wall Chasing Work Progress



Waterproofing – Ninth Floor Work In Progress



Ninth Floor – 1st Coat Wall Putty Work Completed



First Floor – 1st Coat Ceiling Putty Work In Progress



Fifth Floor Wall Tile Laying Work Completed



Wall Tile – Sixth Floor Work In Progress



Floor Tile - Third Floor Tile Laying Work In Progress



**External– Entry Entrance Arch Block Work Completed & Plastering
Work In Progress**



External Plastering Work In Progress

*Thank
you!*
